

## VIII.D Energy Station

### VIII.D.1 Research and Development of a PEM Fuel Cell, Hydrogen Reformer, and Vehicle Refueling Facility

*Edward Kiczek (Primary Contact), Mark Wait, Vincent Cassala, and Dan Hyde*  
*Air Products and Chemicals, Inc.*  
*7201 Hamilton Boulevard*  
*Allentown, PA 18195*  
*Phone: (610) 481-4705; Fax: (610) 706-7463; E-mail: KiczekEF@airproducts.com*

*DOE Technology Development Manager: Sigmund Gronich*  
*Phone: (202) 586-1623; Fax: (202) 586-9811; E-mail: Sigmund.Gronich@ee.doe.gov*

*DOE Project Officer: Doug Hooker*  
*Phone: (303) 275-4780; Fax: (303) 275-4743; E-mail: Doug.Hooker@go.doe.gov*

*Contract Number: DE-FC36-99NV13578*

*Subcontractors:*  
*Plug Power Inc., Latham, NY*  
*City of Las Vegas, Las Vegas, NV*

*Start Date: October 1, 1999*  
*Projected End Date: March 31, 2006*

#### **Objectives**

Design, develop, and demonstrate small on-site H<sub>2</sub> production system for stationary fuel cells and H<sub>2</sub> fuel stations.

- Design, construct, and operate a multipurpose refueling station to dispense hydrogen/compressed natural gas (HCNG) blends, and pure H<sub>2</sub>.
- Design, construct, install and operate a H<sub>2</sub>-fueled stationary 50kW fuel cell
- Maintain safety as a top priority for the fueling station and fuel cell.
- Evaluate operability, reliability, and economic feasibility of integrated power-generation and vehicle-fueling system.
- Obtain adequate operational fuel station data to provide basis of future commercial fueling station designs.

#### **Technical Barriers**

This project addresses the following technical barriers from the Technology Validation section of the Hydrogen Fuel Cells and Infrastructure Technologies Program Multi-Year Research, Development and Demonstration Plan (HFCIT MYRDDP):

- B. Storage – Cost, Performance, Structural Integrity
- C. Hydrogen Refueling Infrastructure – Cost, Availability, Safe Systems
- D. Maintenance & Training Facilities

- E. Codes & Standards – Lack of Adopted Codes and Standards
- I. Hydrogen and Electricity Co-production – Cost / Durability, Permitting, Safety

### **Contribution to Achievement of DOE Technology Validation Milestones**

This project will contribute to achievement of the following DOE technology validation milestones from the Technology Validation section of the HFCIT MYRDDP:

- *Milestone 11 – Validate cost of producing hydrogen in quantity of \$3.00/gge untaxed.* Results achieved and lessons learned in this project will be applied to the Penn State Fueling Station project, assisting progress on this milestone for that project.
- *Milestone 15 – Validate co-production system using 50 kW fuel cell, hydrogen produced at \$3.60/gge and electricity at 84/kW hr.* This report covers the conclusion of demonstration testing of the distributed production of hydrogen for this project. The results validate the capability to achieve this milestone as defined by the HFCIT MYRDDP.

### **Approach**

- Several small-scale, natural gas-based, fuel-processing technologies under development by others were tested. These included partial oxidation (POX), auto thermal reforming (ATR), and steam methane reforming (SMR) technologies. Based on the experience from the testing and the results of an economic analysis, the final technology selected to use was SMR.
- The 50 kW fuel cell stack design was based on existing 7.5 kW reformatate-based stack modules developed for residential power generation. Modifications were made to allow operation on pure hydrogen.
- The fuel station was based on previous H<sub>2</sub> and HCNG fueling station experience.
- Extended duration operation of the fully integrated hydrogen-generation, fuel-cell, fuel station system will be conducted to address robustness, performance, and economic feasibility of this “Energy Station” concept.

### **Accomplishments**

- Achieved satisfactory process operation and product-purity capability with the Hydrogen Generator, with one-button start and load-following capability.
- Achieved aggregate Hydrogen Generator operation of over 4,800 hours.
- Achieved lower heating value (LHV) efficiency of 68%, with hydrogen purity at <1 ppm CO.
- Identified and implemented system improvements under real-world performance and durability testing experience.
- Successfully performed over 200 HCNG blend and hydrogen fuelings.
- Achieved safe operation of the site over the operating period to date.


### **Future Directions**

- Continue to provide the City of Las Vegas (CLV) fleet fueling and fueling demonstration testing through conclusion of current project period. Support CLV fleet expansion as applicable.
- Lessons learned are to be incorporated into the Penn State Hydrogen Fueling Station Project.

## Introduction

Small-scale, on-site hydrogen production technology that can operate on available fuels such as natural gas will be required to provide hydrogen for fueling stations where delivered hydrogen is not readily available. Small-scale, natural gas-based hydrogen reformers are not fully developed, and will suffer from poor economics due to their size and poor utilization rates in the early years of hydrogen vehicle development. One approach to achieving high utilization rates on the reformer is to baseload it with a stationary fuel cell that produces electric power while the intermittent vehicle fueling load is handled by diverting a portion of the hydrogen from the fuel cell to the fuel station. This co-production of hydrogen fuel and electric power is referred to as an "Energy Station." A team of three organizations, Air Products and Chemicals Inc., Plug Power Inc., and the City of Las Vegas (CLV), under the leadership of Air Products, has contributed to this Energy Station demonstration in Las Vegas, Nevada.

Figure 1 is a block diagram of the refueling facility. In addition to the on-site hydrogen generation, a liquid hydrogen supply system was installed to satisfy initial demand for hydrogen at the refueling station, and to provide backup supply for additional system reliability. The hydrogen compression, storage, blending and dispensing system is capable of supplying pre-determined blends of H<sub>2</sub> and compressed natural gas (CNG) to be dispensed to trucks and buses with internal combustion engines (ICE) that have been converted

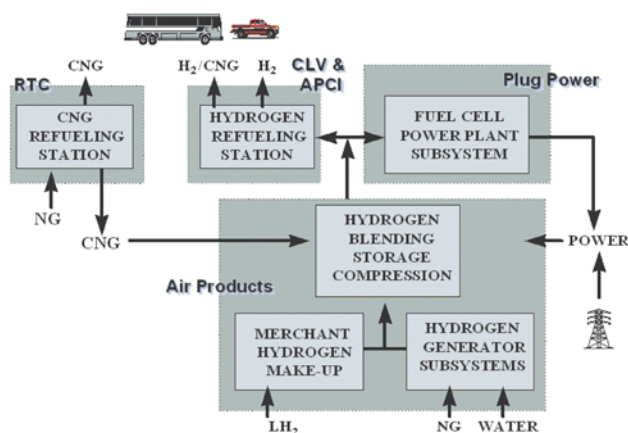

**Figure 1.** Overall Integration System Configuration

to run on HCNG mixtures. The station is also able to dispense pure hydrogen to vehicles. Currently one light-duty vehicle (LDV) and one para-transit bus are being fueled with the HCNG blend.

## Approach

Early in the project, Air Products evaluated various small-scale developmental natural gas reformation technologies via extensive laboratory and field-testing. These technologies included POX, ATR and SMR. Based on the test results, SMR was selected for the fuel processor. The fuel processor was integrated with a pressure swing adsorption (PSA) system supplied by QuestAir to develop the on-site system capable of generating pure hydrogen from natural gas.

Plug Power developed and provided a 50 kW fuel cell for the project. This fuel cell was built by assembling eight 7.5 kW fuel cell stacks that were being developed by Plug Power for the residential power market. The residential system was designed to operate on reformate, and thus modifications were required for the pure hydrogen service in this project. Extensive testing of the fully assembled module at Plug Power's Latham, New York facility was conducted to qualify individual systems and the final system configuration.

This report covers the conclusion of the Hydrogen Generator distributed generation test period. Previous results achieved by Plug Power's 50 kW fuel cell power generation system were considered in evaluating and validating the co-production capabilities of the Energy Station.

## Results

### **Hydrogen Generator**

The Hydrogen Generator was installed, commissioned and placed into operation in the summer of 2002. On-spec hydrogen production, with purity in excess of 99.95%, was established in August 2002. Successful operation of the hydrogen generator was achieved without process modification to the system after delivery of the unit to the site. Since the initial establishment of hydrogen production, the unit has achieved an aggregate run-time of over 4,800 hours. The integrated hydrogen



**Figure 2.** View of the Hydrogen Generator (Left) and Fuel Cell (Right)

generator system controls achieved the full range of expected operability control.

During this period, we continued to test the operation of the Hydrogen Generator. An overall system efficiency (LHV) of 68% was achieved, with hydrogen produced at purities of less than 1 ppm CO.

Further economic analysis of the technology was performed during this period. Based on the economic assumptions provided by the DOE HFCIT MYRDDP, the test results from Las Vegas confirm the technology's ability to achieve an integrated, co-production result of less than \$3.60/kg (gasoline gallon equivalent) cost of hydrogen and 84/kWh cost of electrical power.

Las Vegas provides an excellent real-world performance and durability testing environment. Several improvement opportunities were identified as a result of the operating conditions provided by this Nevada site.

### **Fueling Station**

The Fueling Station segment of the Energy Station consists of liquid hydrogen storage, gaseous hydrogen storage, product compression, HCNG fuel blending, and HCNG and hydrogen fuel dispensing. Since operation of the Fueling Station was established, satisfactory vehicle fueling functionality has been demonstrated. Fueling operations have been performed for both hydrogen fuel cell vehicles and blend HCNG internal combustion engine vehicles. To date over 200 fuelings have been safely performed.



**Figure 3.** View of the Fuel Station

During this period, the fueling pressure was upgraded from a 250 Bar (3,600 psig) hydrogen fueling capability to a 350 Bar (5,000 psig) fueling capability. This upgrade to the hydrogen fueling was made in April 2005 and continues to operate reliably.

The DOE Safety Panel reviewed the project and the site in March 2004. A better than satisfactory assessment was achieved from this review.

### **Conclusions**

- The Energy Station is a viable operational concept. The fuel cell provided demand for hydrogen during low levels of vehicle fueling demand.
- DOE HFCIT MYRDDP targets are obtainable with the technologies used for this demonstration. Further adoption of the technologies is necessary to realize the economic factors applicable to achieving the targets.
- This project has provided a significant source of development opportunities, given that it is an applied technology demonstration in a real-world environment.

### **FY 2005 Publications/Presentations**

This project was presented at the following meetings:

- DOE Regional Meeting in Annapolis, MD – 2004
- Annual NHA Meeting – March 2005
- SAE Annual Meeting – 2004
